



# AI infrastructure, built in phases

Mead, Oklahoma

A founder-backed B300 deployment.  
Capital released against commercial evidence.



INVESTOR DISCUSSION / SEPTEMBER 2026

RUNWAY PRODUCT CONCEPT / NVIDIA REFERENCE / NOT THE SELECTED SUPERMICRO SYSTEM

# A stronger foundation. A staged decision.

---

## \$6.00m

initial founder capital, owner-reported

Management also intends to fund the overage. The proposal can be developed without treating \$6m as a fixed funding ceiling.

Three sources of potential value

Long-term site access

Behind-the-meter power strategy

Dedicated B300 compute capacity

The investment decision depends on complete delivery costs, binding customer payments and agreed investor rights.

Founder availability and willingness are reported, not verified transfers. Customer discussions are active; no signed revenue or definitive updated return is established.

# Founder capital changes the funding path

| CURRENT BASIS                   | WHAT IT MEANS                                                                                                        |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------|
| \$6,000,000 initially           | Owner reports the funds are available. Confirm contribution form, timing and transfer into the project.              |
| Overage willingness             | Owner intends to personally cover additional costs. The amount is to follow the completed budget.                    |
| Existing property and buildings | Reported paid off and held by BC LLC. Property value is separate from spendable project cash.                        |
| Outside investment              | Optional structure remains open. No fixed raise, valuation, equity percentage or return entitlement is offered here. |

More funding can support delivery; it does not by itself improve operating profit or investment return. Source: management interview, 11 Sep 2026.

# Customer interest is the starting point

---

## Active discussions

Two commercial channels are under discussion. Management reports a potential 180-B300 requirement and a separate resale/offtake opportunity.

## The current commitment level

0 signed customer contracts

0 paid pilots established

No agreed minimum receipts

**Prospective capacity informs the sales process.**  
**Signed payment terms determine procurement.**

Customer reports have not been independently verified. Identities and private discussions are omitted. A potential 180-GPU request is not an order or an expansion commitment.

# Turn discussions into bankable payments

TERM TO ESTABLISH

COMMERCIAL QUESTION

**Payment counterparty**

Which legal entity owes SmartTec money, and what credit support stands behind that obligation?

**Minimum receipts**

What must be paid for compliant reserved capacity, even when resale or workload demand falls short?

**Net realized price**

Does \$6.50/GPU-hour describe host receipts, end-customer price or a negotiated service rate?

**Acceptance and exit**

Agree workload tests, start date, term, deposit, termination, service credits and remedies.

Proposed negotiation topics. No deposit, minimum payment or take-or-pay contract has been established. Marketplace listing access alone does not answer these questions.

# A long-term home for the operation

## 50 years

site-use agreement, signed status confirmed by management

Management identifies BC LLC as landholder, with an ownership connection to the CEO. The property is reported paid off.

39.39 acres / 5,035 sq ft gross A + C area

## 1% annually

Management describes a payment to BC LLC of 1% of profit remaining after expenses.

Review the written accounting definition, premises, termination, improvements and investor or lender rights.

Owner record: agreement signed, document and title unreviewed. Site access does not imply SmartTec property ownership or investor collateral. Runway campus concept.

# Power is a potential operating advantage

## <7 cents

per kWh, reported by management

### Solar + batteries + gas generation

Management reports a supply agreement.  
Its economic advantage must be  
demonstrated at the actual delivered  
service level.

### Evidence still required

Exclusive continuous kW

Service availability date

Fuel and maintenance obligations

Losses, replacements and equipment costs

Interruption and recovery terms

The rate is not a verified all-in tariff. Shared OG&E service is recorded separately; it does not establish exclusive capacity. Runway power concept, not installed equipment.

# Eight complete Supermicro B300 systems

---

## \$5.36m

8 systems x \$670,000

64 proposed GPUs

60 saleable + 4 financial reserves

Direct liquid cooling

Owner-reported complete-system scope

Eight B300 GPUs

Dual Intel Xeon 6776P CPUs

NVSwitch fabric


Networking and storage

NVIDIA software stack and support

Supplier price and scope are management inputs. Exact configuration is private and unreviewed. Support term, external fabric, taxes, freight and installation still need reconciliation.

# 60 saleable GPUs. Four financial reserves.

EIGHT SYSTEMS / EIGHT GPUS EACH

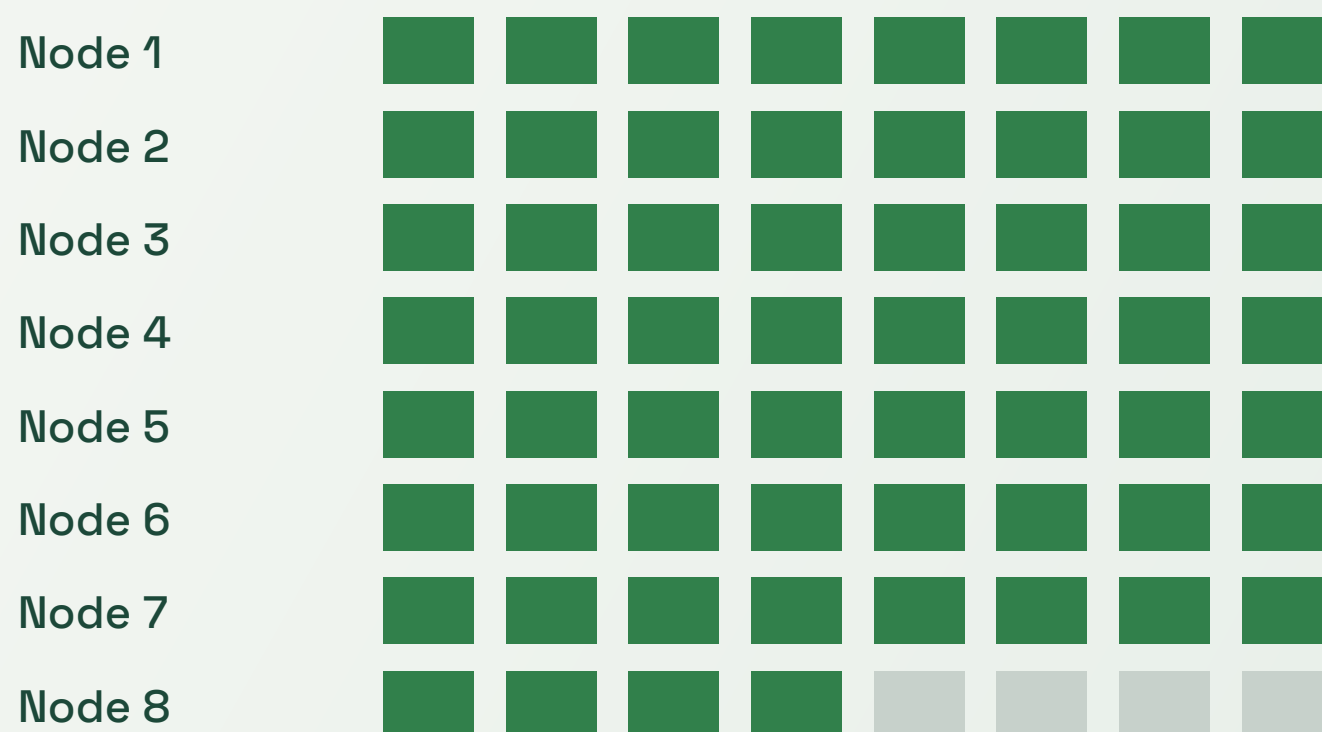

## 60 saleable

Revenue uses the 60 saleable GPUs.  
All 64 are in the proposed purchase.

## Reserve is not full redundancy

Four GPUs cannot replace one complete eight-GPU node. Whole-node workloads, failures and recovery need validation.

Illustrative financial allocation, not an approved scheduling or spare-parts topology. Heat and electrical design must account for the complete proposed fleet.

# One building. Two controlled cooling loops.

## 225 kW

net cooling-duty screening target  
per full-duty chiller

Two full-duty chillers and two CDUs are retained in the initial comparison. One unavailable unit must not remove the required cooling duty.

### Warm server-coolant circuit

CDUs isolate and control the compatible direct-liquid-cooled server loop.

### Separate residual-air cooling

Price rear-door cooling against complete new room cooling. The building has no working air conditioning to reuse.

225 kW is an engineering allowance, not confirmed OEM load:  $(8 \times 20 + 20 \text{ ancillary} + 5 \text{ pump}) \text{ kW} \times 1.20 = 222 \text{ kW}$ , rounded up. Component redundancy is not facility certification.

# Cooling: compare complete installed scope

---

**\$1,083,600**

Full-scope analyst comparison. Two chillers, two CDUs, dry coolers, four active rear doors and installation allowances. Includes 20% contingency.

**\$831,600**

Lower-cost sensitivity. Assumes a \$100,000 chiller pair and defers \$70,000 of separate dry coolers. Other allowances and 20% contingency remain.

---

**Neither amount is minimum pricing or an approved contractor bid.**

Compare new and warranted refurbished equipment. Keep summer duty, residual-air cooling, controls, installation and commissioning in scope.

Savings are arithmetic, not verified quotations. Reprice energy use when dry cooling is deferred. The team reports a mechanical contractor, electrician and plumber are available.

# A funding bridge, before the remaining scope

| CURRENT PLANNING INPUT                 | FULL-SCOPE  | LOWER-COST  |
|----------------------------------------|-------------|-------------|
| Eight complete B300 systems            | \$5,360,000 | \$5,360,000 |
| Cooling allowance                      | \$1,083,600 | \$831,600   |
| Retained startup/acquisition allowance | \$566,000   | \$566,000   |
| Retained opening operating reserve     | \$264,501   | \$264,501   |
| PARTIAL INITIAL FUNDING                | \$7,274,101 | \$7,022,101 |
| Above initial \$6m founder funding     | \$1,274,101 | \$1,022,101 |

Excludes unknown non-cooling site work, reserve revision and later capital calls. Replace the earlier \$652,800 combined site allowance; do not add it again. Reconcile scope overlaps.

# Paid GPU-hours drive the revenue case

---

**\$2.85m**

illustrative annual gross billings

60 saleable GPUs x 20 paid hours/day  
x \$6.50/GPU-hour x 365 days

The deductions are material

Unpaid hours and customer collections

Platform or sales charges

Power, cooling and connectivity

People, support and maintenance

BC LLC payment, taxes and reserves

Gross arithmetic is not booked revenue, a forecast or investor profit. 20 paid hours/day equals 83.3% of saleable capacity. Actual utilization, net price and fees remain unresolved.

# The return case must be rebuilt

---

## Updated ROI: not established

The new cooling scope and property payment change the cost basis. Publishing an exact return before completing that basis would overstate what is known.

---

### Complete the cash requirement

Add non-cooling work; match tax, freight and installation scope; then size working capital and future reserves.

### Reconcile the operating model

Use net customer receipts, seasonal power, maintenance, site payments, taxes and a funded hardware-life policy.

Founder willingness to cover costs supports funding flexibility. It does not cure weak project returns. No updated NPV, payback date or investor distribution is asserted.

---

# Earlier returns are a historical diagnostic

---

What the previous illustration showed

**-\$0.67m**

NPV at an assumed 15% annual hurdle

Positive operating cash did not compensate for the previous modeled capital cost and timing.

Why it is not current underwriting

The earlier model used a \$652,800 combined site allowance. It did not include the newly itemized cooling comparison, unresolved non-cooling scope or BC LLC payment.

**Old ROI, payback and price thresholds must not be applied to this updated plan.**

Historical owner-deployment scenario only, reproduced by the monthly engine. This deck deliberately does not present the earlier 28.7% ROI as the current investment return.

# Underwrite resilience before buying scale

---

| CASE                          | WHAT TO TEST BEFORE A PURCHASE                                                                           |
|-------------------------------|----------------------------------------------------------------------------------------------------------|
| Supported operating case      | Signed net price and payment terms; validated cost scope; realistic commissioning and collection timing. |
| Lower demand and pricing      | Fewer paid hours, rate pressure, customer concentration, churn and nonpayment.                           |
| Delivery and operating stress | Delayed launch, higher power/demand costs, repair events, outage credits and added working capital.      |
| Hardware-life and exit stress | Overhaul versus replacement, funded reserves, resale downside, wind-down costs and investor cash rights. |

Use the agreed return hurdle and investor structure after the cost model is complete. No fleet size or uncontracted selling price is a substitute for these tests.

# Release capital against evidence

| GATE                 | EVIDENCE                                                                          | CAPITAL CONSEQUENCE                                |
|----------------------|-----------------------------------------------------------------------------------|----------------------------------------------------|
| 1 Commercial         | Paid validation and enforceable payment terms from a creditworthy counterparty    | Size the first order from supported demand.        |
| 2 Technical          | Exact load/flow requirements, full installed budget and deliverable power/network | Approve the delivery scope and cash reserve.       |
| 3 Procurement        | Final price, payment milestones, warranty, delivery and acceptance terms          | Place orders with documented release controls.     |
| 4 Service acceptance | Load tests, failure tests, customer acceptance and operating readiness            | Start contracted service; expand against receipts. |

A proposed control framework, not completed milestones or an approved procurement commitment. Staged orders remain subject to supplier and customer agreement.

# Dates follow acceptance and lead times

| WORKSTREAM           | CURRENT BASIS                                            | NEXT ACCEPTANCE                                       |
|----------------------|----------------------------------------------------------|-------------------------------------------------------|
| Building preparation | Single-building deployment planned; new cooling required | Survey, layout, permits and contractor scope.         |
| Power                | Owner-reported agreement and shared electrical service   | Exclusive continuous kW and commissioning.            |
| Cooling and network  | Design concepts and contractor resources identified      | Installed systems, measured duty and throughput.      |
| Compute service      | 64-GPU planning fleet; customer discussions active       | Workload proof, signed terms and customer acceptance. |
| Expansion            | Potential demand under discussion                        | Evidence-backed next order and available capacity.    |

Earlier construction, utility and fiber dates are targets to reconfirm, not completed work. No updated service launch date is committed in this presentation.

# The team carrying the project forward

---

**Syed Hussain**

Chief Executive Officer

---

**Yasir Jahangir**

Chief Technology Officer

---

**Muhammad Siddiqui**

Chief Operating Officer

---

**Ryan**

Director of Operations

---

**Daniel**

Chief Financial Officer

---

**Ken**

Legal

---

**Javed Iqbal, PhD**

Strategic Advisor

---

**Shahb Kazmi**

Senior Advisor

---

**Ali Askara**

Graphics and Media Relations

---

Names and roles are management-supplied. Complete professional names where abbreviated, verified project experience and commitment levels remain part of diligence.

# Define what an investor actually receives

---

## Capital and economic rights

Agree the funded entity, founder equity or loan treatment, valuation, ownership, distributions and capital-call obligations. No terms are fixed here.

## Site and related-party protections

Review BC LLC site rights and annual profit payment. Confirm improvements, termination, assignment, permitted financing and related-party approvals.

---

## Reporting and oversight

Monthly receipts, paid utilization, outages, costs and reserve coverage. Capital releases tied to documented milestones and agreed approval rights.

Governance proposals require agreement and documentation. Paid-off property is not automatically SmartTec equity or investor collateral. No preferred return or waterfall is promised.

# Give each open item an accountable owner

| PROPOSED LEAD                      | DELIVERABLE                                                                                               |
|------------------------------------|-----------------------------------------------------------------------------------------------------------|
| CEO / COO                          | Customer counterparty, paid workload evidence, minimum payments and staged capacity commitments.          |
| CTO / Operations                   | Supplier interfaces, liquid-cooling requirements, network design, service tests and operating procedures. |
| Mechanical / Electrical / Plumbing | Complete installed pricing, design coordination, site scope and tested commissioning.                     |
| CFO / Legal                        | Founder contribution documents, BC agreement review, full model, reserves and investor terms.             |

Responsibilities are proposed for confirmation. Contractor availability is owner-reported; qualifications, scope, prices and acceptance remain to be established.

# Expand only when the next phase earns it

---

## 64 GPUs under review

Eight systems form the current planning case. Customer commitments and the completed cost model determine what is purchased and when.

## 180 GPUs discussed

Management reports potential customer interest at this scale. It is not signed demand, funded expansion or approved site capacity.

---

## Owned compute or customer-owned hosting

Compare the capital required, customer credit, service obligations and net receipts of each route. No hosting or manufacturing income is included in current revenue arithmetic.

Runway campus concept, not installed buildings or approved expansion plans. Future manufacturing and energy development require separate budgets and decisions.

# The risks have specific evidence tests

| EXPOSURE                 | REQUIRED EVIDENCE                                                                                  |
|--------------------------|----------------------------------------------------------------------------------------------------|
| Commercial               | Signed payment obligations, credit support, workload requirements and customer acceptance.         |
| Power and cooling        | Delivered capacity, complete tariff scope, summer duty, failure testing and annual operating cost. |
| Equipment and operations | Complete system scope, external fabric, support term, staffing, security and funded replacements.  |
| Property and governance  | Reviewed BC agreement, title position, exact payment base, contribution form and investor rights.  |
| Financial information    | Complete sources and uses, reconciled costs, downside cases and company financial records.         |

Development-stage discussion material. Capital remains at risk. No audited SmartTec financial statements, investment approval or funding guarantee is represented.

# Reconcile costs before calculating returns

---

## Energy and maintenance

The previous model used PUE 1.4 and 7 cents/kWh, including facility overhead energy. Reconcile seasonal cooling power and site charges; do not add cooling electricity twice.

## Commercial and property costs

Clarify host net receipts versus end-customer pricing, fees and collections. Apply the written BC LLC profit definition and agreed tax, reserve and distribution treatment.

---

## Reserve policy is part of the model

The retained \$264,501 opening reserve and \$25,000/year cooling-service allowance are planning inputs. Recalculate and add only uncovered scope.

No revised operating-expense total or five-year cash schedule is asserted. Exact supplier support coverage, other site work and later capital requirements remain open.

# Evidence register

---

## Management inputs / 11 Sep 2026

Founder capital and overage willingness

Supermicro complete-system price and scope

BC LLC signed-site-agreement status

One-building deployment; no working HVAC

Active customer discussions; no signed terms

## Analyst work / preliminary

Itemized cooling comparison, arithmetic funding bridge and historical monthly cash model. No contractor bids.

External sources provide product or market context only. Owner facts are reported; private contracts, quote terms and funding have not been independently reviewed.

## External context, not project verification

Supermicro liquid-cooled Blackwell portfolio

Vast.ai hosting and marketplace context

New chiller manufacturer pricing context

Refurbished chiller testing and warranty

SmartTec investor room and planning basis

# Build the evidence. Then commit the capital.

---

## A founder-backed path to B300 capacity

Complete the delivery budget. Convert customer interest into payment obligations. Review power and site rights. Rebuild the return case around those terms.

Investment terms follow the completed case.

**Yasir Jahangir**

Chief Technology Officer

yasir@smarttec.dev  
918-520-3823

[smarttec.dev/investors](https://smarttec.dev/investors)

8460 US 70, Mead, Oklahoma 73449. Discussion material; no definitive investment terms or return are offered. Background: Runway campus concept.
