

AI infrastructure, built in phases

Mead, Oklahoma

A development-stage investment in GPU compute
and a behind-the-meter power strategy.



A contract-first AI compute opportunity

39.39

acre legal parcel in Mead, Oklahoma

SmartTec.dev LLC operates under SmartTec Holdings LLC. Z1Power provides the parent battery-company context.

A focused compute opportunity

Dedicated B300 capacity for customers whose workloads, credit and minimum payments justify procurement. Complete costs and power terms determine fleet size.

Power economics

Management reports a solar, battery and gas supply agreement below 7 cents/kWh. Firm capacity and full cost coverage remain under review.

Development-stage discussion. Owner reports underpin property, organization and power statements. Signed customer demand is unverified.

The investment decision under review

\$6.95m

illustrative total project funding

60 saleable B300 GPUs plus four reserves.
\$6.84m initially, plus about \$107,000 in
modeled later calls.

The immediate invitation is investment
diligence. Final raise, valuation and investor
rights remain open.

Before procurement

Enforceable customer payments

Reviewed power and engineering

Complete procurement and operating costs


Agreed investor and reserve policies

Current case: 28.7% total five-year ROI and
approximately -\$674,000 NPV at the assumed
15% annual hurdle.

Illustrative funding is not an agreed raise or offered return. Commercial improvements must produce acceptable downside economics before equipment commitment.

Power demand creates a large backdrop

Global data-center electricity use

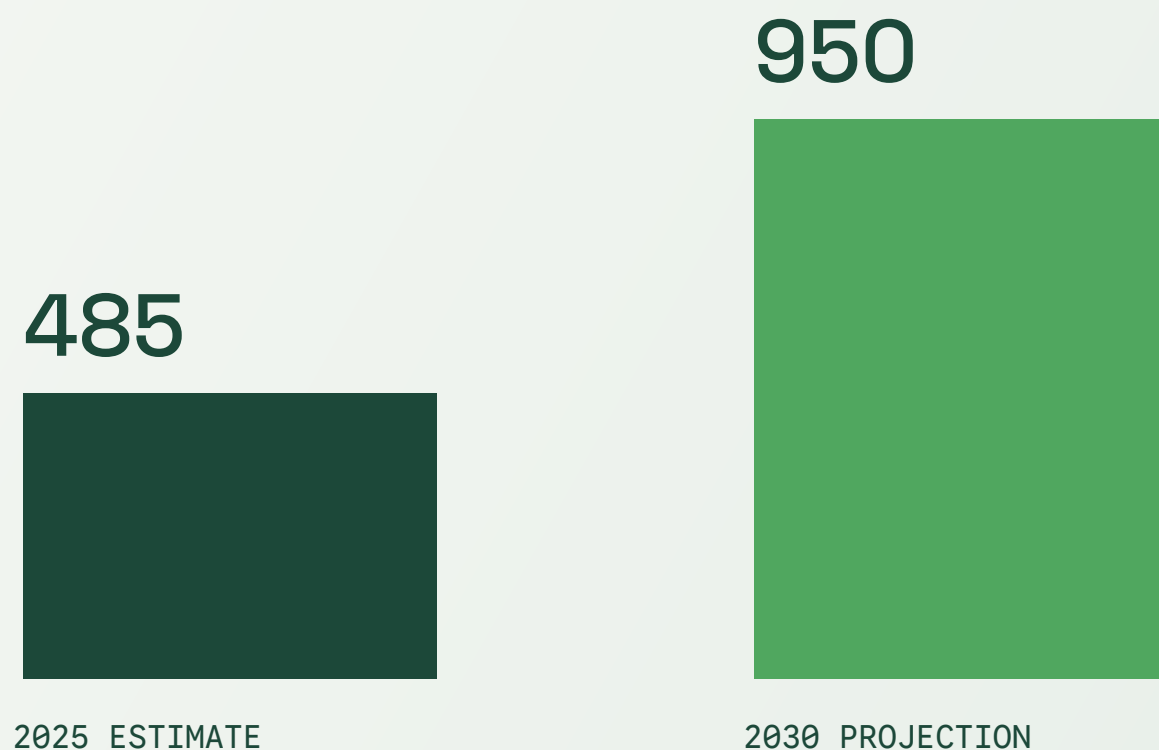

TWh / year

Source: IEA, Key Questions on Energy and AI (2026), executive summary. Global demand does not establish SmartTec bookings or market share.

Local revenue depends on execution

The IEA's 2026 outlook projects roughly twice the global data-center electricity use by 2030.

SmartTec must turn its own available power, commissioned infrastructure and workload performance into paying customer contracts.

The Mead campus

5,035

sq ft gross data-center building area

Building A: 1,500 sq ft

Building C: 3,535 sq ft

Building B adds 2,083 sq ft for batteries, utilities and storage. Gross building area does not establish IT capacity.

8460 US 70, Mead, OK 73449

The campus concept separates existing compute structures from proposed manufacturing and energy development.

Two proposed 30,000 sq ft factories address inverter manufacturing and battery assembly. Solar and storage remain separate development scopes.

Owner record, 10 Sep 2026. Legal acreage: 39.39. Legacy survey tract annotations total 39.21 acres. Title, rights and permitted use require diligence.

Behind-the-meter power strategy

<7¢

per kWh, reported by management

Management reports a supply agreement using solar, batteries and gas generators.

The model uses 7¢/kWh. The team is confirming continuous reserved kW, service date and fuel, maintenance and equipment obligations.

Energy input is conditional, not a verified all-in tariff. Shared O&M; service is recorded separately. Image: Runway concept artwork, not installed equipment.

Capacity and commissioning evidence

SYSTEM	CURRENT BASIS	REQUIRED ACCEPTANCE
Electrical	3,000 A / 208 V / three-phase owner-reported shared service	Usable exclusive kW, voltage conversion, protection and commissioning
Cooling	Two-loop design concept	Final OEM loads, heat rejection, controls and commissioning tests
Connectivity	Dobson fiber target 8 Oct - 5 Nov 2026	Installed service, measured throughput and actual carrier terms
Resilience	Four spare GPUs in the 64-GPU case	Node failure, network failure, power transfers and recovery procedures

Planning records and engineering allowances. Four GPUs do not replace a complete eight-GPU node. No uptime certification or approved site capacity is claimed.

B300 leads at the supplied prices

OWNER INPUT	B300	RTX 6000
GPU-hour rate	\$6.50	\$1.50
Eight-GPU system	\$670,000	\$170,000
Per-GPU allocation	\$83,750	\$21,250

B300 suits the primary owned-compute study. RTX needs a workload and pricing case that justifies its investment.



Owner inputs, 10 Sep 2026. OEM scope and support unverified. RTX: PRO 6000 Blackwell Server Edition. Runway product concept uses NVIDIA DGX B300 visual reference; selected OEM pending.


The proposed customer offer

OFFER ELEMENT	PROPOSAL AND EVIDENCE
Service	Dedicated B300 capacity. Workload, networking, storage, security and support scope to be agreed.
Price assumption	\$6.50 per GPU-hour. Signed customer pricing and minimum payments have not been supplied.
Paid-volume target	1,200 GPU-hours/day: 60 saleable GPUs x 20 paid hours. 83.3% of saleable capacity, from month 4.
Proof before procurement	Paid workload validation, customer credit review, minimum payments, cancellation terms and costed service credits.

These are proposed terms, not bookings. Meeting 1,200 paid GPU-hours/day at \$6.50 alone still fails the assumed 15% annual project hurdle.

What 60 + 4 reserve GPUs actually means

EIGHT SYSTEMS / EIGHT GPUS EACH

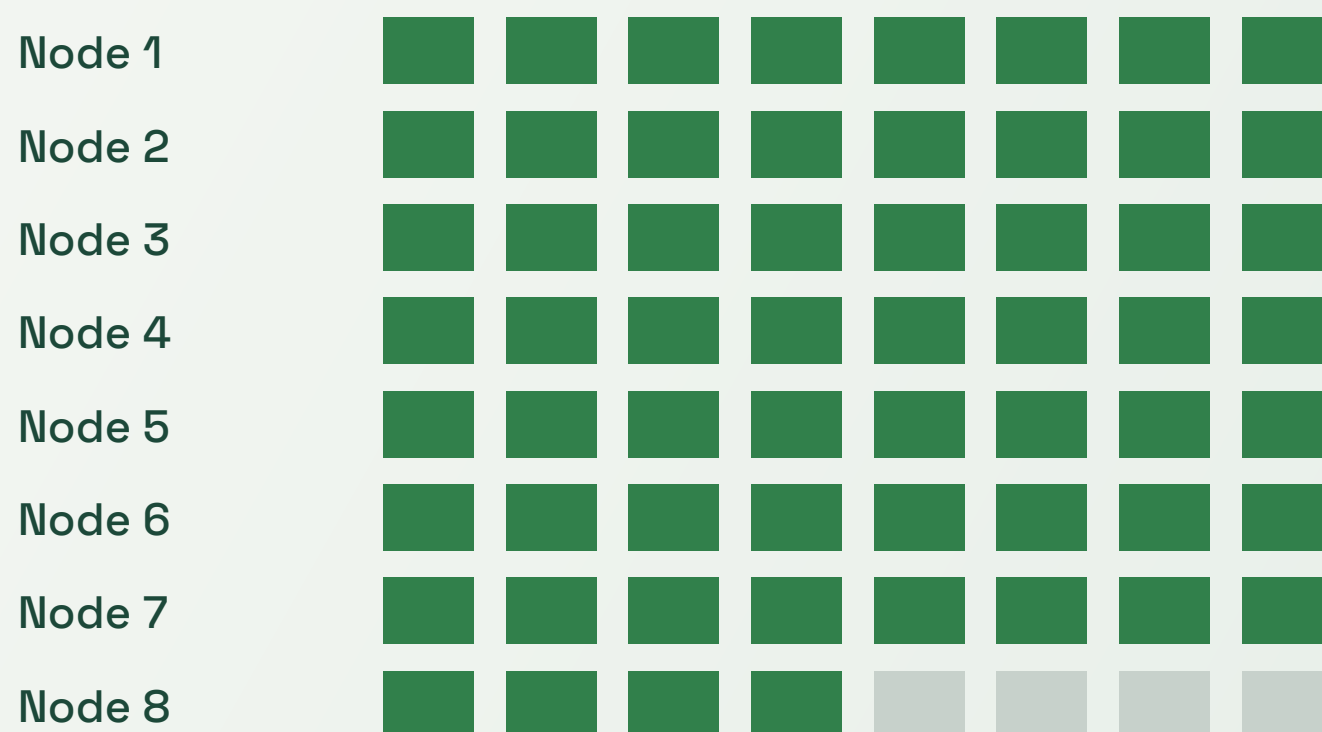

60 saleable

Seven fully saleable nodes and four additional saleable GPUs in node 8.

4 reserved

Four reserved GPUs cannot replace an entire eight-GPU node. Scheduling and failure recovery need OEM validation.

\$5.36m hardware / 159.6 kW modeled IT peak

GPU count chart illustrates financial allocation, not validated operational topology. This alternative is separate from the earlier two-RTX/one-B300 starter concept.

Monthly cash generation can be positive

NORMALIZED 30-DAY OPERATING MONTH

USD

60 GPUs x 20 paid hours x \$6.50 x 30 days	\$234,000
Receipts after 98% collection and 10% fees	\$206,388
Electricity at 7¢/kWh and PUE 1.4	\$8,538
Other operations, network and demand costs	\$35,427
Operating cash before capital spending	\$162,423

Illustrative early operating month. Operating cash excludes equipment/site acquisition, overhaul, tax and investor distributions. Calendar-month results vary.

Capital covers more than GPUs

\$6.84m

initial modeled funding

Plus approximately \$106,584 in later capital calls.

The final raise depends on full quotes, customer terms, engineering and the agreed investor structure.

INITIAL USE	USD
Eight B300 systems	\$5,360,000
Site work and contingency	\$652,800
Startup and acquisition allowance	\$566,000
Opening operating reserve	\$264,501


Five-year cash model

USD THOUSANDS	YEAR 1	YEAR 2	YEAR 3	YEAR 4	YEAR 5
Gross billings	2,129	2,855	2,847	2,847	2,847
Collected receipts, net of fees	1,878	2,518	2,511	2,511	2,511
Operating expenses	503	545	561	578	595
Operating cash	1,375	1,973	1,950	1,933	1,916
Later capital spending	0	0	0	536	0
Net distributions less calls	1,375	1,973	1,950	1,397	2,140

Five-year net cash profit: \$1.99m Total five-year ROI: 28.7%

Year 1: Oct 2026-Sep 2027, with sales from Jan 2027. Initial funding excluded from table. Year 4 includes overhaul. Year 5 releases reserve after exit costs.

Capital recovery takes time

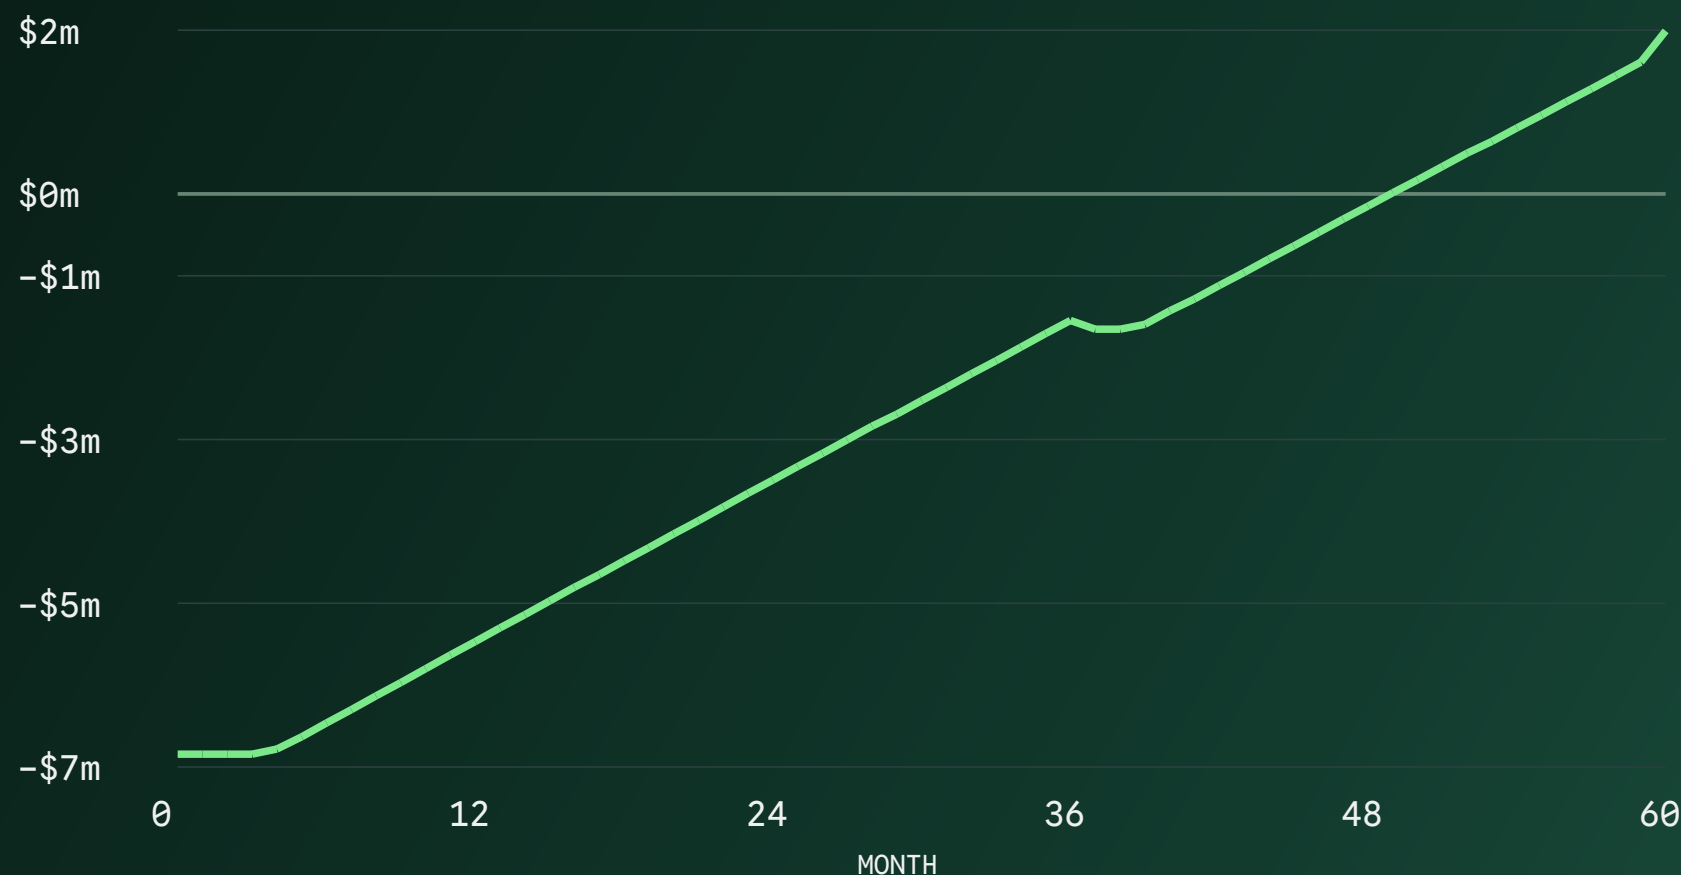

Month 37

\$536,000 overhaul. About \$107,000 of additional capital is called after earlier distributions.

Month 49

Modeled capital payback. The five-year ending net cash profit is \$1.99m.

Cumulative distributions minus contributions, including initial funding, later calls and terminal reserve release. Proposed overhaul-reserve policy still requires modeling and agreement.

Fleet size does not guarantee a strong return

B300 FLEET / 20 PAID HOURS	TOTAL FUNDING	5-YR PROFIT	NPV AT 15%
24 / no reserve	\$2.77m	\$0.17m	-\$0.73m
60 + 4 reserve	\$6.95m	\$1.99m	-\$0.67m
72 / no reserve	\$7.77m	\$3.31m	\$7,361

72 GPUs barely meet the assumed annual hurdle.

Its positive NPV is less than 0.1% of total funding and fails the tested downside cases.

912 configurations: 8-128 GPUs, B300/RTX/mixes, reserve variants and 18/20 paid hours. At 18 hours, none passes. Total ROI and annual discount rate differ.

Price and procurement terms change the result

\$7.03 / GPU-hour

At \$670,000 per eight-GPU B300 system, the 60 + 4 case reaches the 15% hurdle at approximately this flat rental price.

\$604,000 / system

At \$6.50 per GPU-hour, approximately this eight-GPU B300 purchase price reaches the same hurdle, with hardware-linked costs recalculated.

A smaller 24-GPU option

At 20 paid hours/day, approximately \$7.93/hour meets the hurdle with no reserve. At \$6.50/hour, total five-year ROI is about 6%.

Alternative sensitivities, not agreed prices. All cases assume 20 paid hours/day after month 3. Thresholds leave little cushion and need stronger contracted terms.

Downside resilience remains the decision gate

60 + 4 B300 CASE

NPV AT 15%

20 paid hours/day, flat \$6.50 pricing	-\$0.67m
--	----------

18 paid hours/day, flat pricing	-\$1.51m
---------------------------------	----------

20 hours, 10% annual rental-price decline	-\$1.93m
---	----------

20 hours, another \$10,000/month operating cost	-\$1.15m
---	----------

20 hours, full hardware replacement in month 37	-\$3.81m
---	----------

One change at a time. Replacement stress substitutes 100% of original GPU-system cost for the 10% overhaul. No efficiency gain, resale or extra revenue assumed.

Execution milestones

MILESTONE	CURRENT TARGET / REQUIREMENT	CAPITAL RELEASE EVIDENCE
Construction start	24 September 2026 owner target	Defined scope and approved contractor budget
Transformer commissioning	8 October 2026 owner target	Electrical acceptance and exclusive capacity
Dobson fiber delivery	8 October - 5 November 2026 target	Carrier acceptance and performance tests
Compute commissioning	After power, cooling and network acceptance	Workload validation and support readiness
Revenue and expansion	Model sales begin January 2027	Paid commitments and collected receipts

Targets reflect the 10 Sep 2026 owner record and are not completion claims. The financial start date is an assumption, distinct from utility and carrier targets.

Leadership and advisory team

Syed Hussain

Chief Executive Officer

Yasir Jahangir

Chief Technology Officer

Muhammad Siddiqui

Chief Operating Officer

Ryan

Director of Operations

Daniel

Chief Financial Officer

Ken

Legal

Javed Iqbal, PhD

Strategic Advisor

Shahb Kazmi

Senior Advisor

Ali Askara

Graphics and Media Relations

Names and roles supplied by management. No independently verified track records or biographies are represented.

Accountability before capital release

PROPOSED LEAD	DELIVERABLE FOR THE INVESTMENT DISCUSSION
CEO / COO	Qualified customers, paid workload evidence and enforceable minimum-payment terms.
CTO / Operations	Exact OEM specification, power and cooling acceptance, network tests and service-readiness plan.
CFO / Legal	Complete project costs, entity/property rights, cash controls and proposed investor documentation.
Investment committee	Review downside economics and agree procurement conditions, reserves and milestone-based funding.

Responsibility framework proposed for management confirmation. No committee appointment, authority, biographies or investment approvals are implied.

A proposed investment framework

Funding scope

The 60 + 4 illustration requires \$6.84m initially and about \$6.95m including later modeled calls. Final raise size, valuation and ownership terms remain open.

Proposed investor controls

Release capital against signed procurement and commissioning milestones. Report cash collections, paid hours, downtime, operating costs and reserve coverage monthly.

Property and related-party rights

The owner reports \$2m gross property value. Title, debt, valuation and rights held by the investment entity require review. No collateral value enters GPU returns.

Governance proposals require agreement and documentation. The model has no debt and no negotiated investor waterfall, preferred return or tax treatment.

Expansion follows demonstrated demand

Compute first

Validate a paid workload and establish reliable service. Choose an initial fleet supported by complete costs and enforceable minimum payments.

Manufacturing and energy development

Proposed inverter manufacturing, battery assembly, solar and storage each need their own budget and approval.

Customer-owned hosting remains an alternative for separate review. No hosting leases or revenue are assumed.

No manufacturing, electricity resale, land appreciation or speculative terminal valuation supports the GPU return model.

Runway campus concept, not approved plans. The reported power agreement does not establish ownership of generation assets or a construction budget.

Investment risks and information limits

EXPOSURE	EVIDENCE NEEDED BEFORE INVESTMENT
Demand and rental pricing	Paid commitments, credit quality, renewal economics and service-credit limits
Power and engineering	Executed supply terms, continuous kW, cost inclusions and commissioned systems
Equipment and operations	Complete OEM quotes, useful life, support, staffing, security and software costs
Property and governance	Title, debt, permits, related-party rights, cap table and investor documents
Financial evidence	Company financial statements and actual operating records for diligence

Discussion material, not definitive offering terms. Projections are conditional and capital is at risk. This deck contains no audited SmartTec financial statements.

Financial assumptions

Revenue and equipment

60 saleable B300 GPUs plus four reserves. Eight systems at \$670,000 each. \$6.50/GPU-hour, 20 paid hours/day after month 3, flat pricing, 98% collection and 10% selling fees. All equipment purchased upfront.

Cash timing and return

Five years from October 2026. Six-month opening operating reserve. \$536,000 overhaul in month 37. \$40,000 exit cost and zero resale. Costs escalate 3% annually. No debt, tax effects or agreed distribution waterfall.

15% annual discount hurdle

NPV discounts project cash flows at 15% annually. Total ROI = (total distributions - total contributions) / total contributions, across five years. IRR is omitted for potentially ambiguous cash flows.

Source: SmartTec owner-deployment model and monthly ROI engine. These are planning assumptions, not verified costs, contracted utilization or guaranteed returns.

Operating-cost assumptions and sources

Operating-cost basis

\$23,200/month fixed operating allowance

\$8,075/month network allowance

\$4,152/month demand allowance

7¢/kWh energy and PUE 1.4

B300 node planning load: 19.7 kW peak and 15 kW average. Supporting IT adds 2 kW peak and 1 kW average.

Source register

Management record and financial model

IEA 2026: Key Questions on Energy and AI

NVIDIA DGX B300 facility planning reference

Site and team facts: owner record dated 10 Sep 2026 and supplied BM Surveying plat dated 28 Dec 2025.

Fixed costs include \$9,000 shared operations, \$800 system allowance and \$13,400 maintenance. DGX is a power reference, not the selected OEM. Sources checked 11 Sep 2026.

The investment diligence discussion

A fleet sized to paid demand

Review the power agreement, complete supplier pricing, customer commitments and investor structure with SmartTec. Agree procurement conditions before equipment capital is committed.

The fleet and final raise follow the evidence.

Yasir Jahangir

Chief Technology Officer

yasir@smarttec.dev
918-520-3823

smarttec.dev/investors

8460 US 70, Mead, Oklahoma 73449. Review the model and supporting documents in the investor room. Background: Runway campus concept, not existing buildings.
