



AI infrastructure, built in phases

Mead, Oklahoma

A proposed founder-backed B300 deployment.
A customer-led strategy for staged growth.



INVESTOR DISCUSSION / SEPTEMBER 2026

RUNWAY PRODUCT CONCEPT / NVIDIA REFERENCE / NOT THE SELECTED SUPERMICRO SYSTEM

Founder-backed AI infrastructure in Mead

\$6.00m

initial founder capital, owner-reported

Management also intends to fund the overage. The proposal can be developed without treating \$6m as a fixed funding ceiling.

Three sources of potential value

Long-term site access

Behind-the-meter power strategy

Dedicated B300 compute capacity

The investment decision depends on complete delivery costs, binding customer payments and agreed investor rights.

Founder availability and willingness are reported, not verified transfers. Customer discussions are active; no signed revenue or definitive updated return is established.

Founder funding position

CURRENT BASIS	WHAT IT MEANS
\$6,000,000 initially	Management reports funds available. Contribution form, timing and transfers into the project remain unverified.
Overage willingness	Management intends to personally fund additional costs. The amount depends on the completed project budget.
Existing property and buildings	Reported paid off and held by BC LLC. Property value is separate from spendable project cash.
Outside investment	Optional structure remains open. No fixed raise, valuation, equity percentage or return entitlement is offered here.

Management-reported funding availability and overage intent, 11 Sep 2026. Funds and transfers have not been independently verified; investment economics remain open.

Commercial pipeline and current commitments

Active discussions

Two commercial channels are under discussion. Management reports a potential 180-B300 requirement and a separate resale/offtake opportunity.

The current commitment level

0 signed customer contracts

0 paid pilots established

No agreed minimum receipts

The proposed procurement strategy links capacity to contracted workloads and payment terms.

Customer reports have not been independently verified. Identities and private discussions are omitted. A potential 180-GPU request is not an order or an expansion commitment.

Proposed customer agreement structure

AGREEMENT AREA	PROPOSED SCOPE
Payment counterparty	The paying legal entity, its payment obligations and the credit support available to SmartTec.
Minimum receipts	Minimum payments for compliant reserved capacity, including periods of lower resale or workload demand.
Net realized price	The distinction between net host receipts, customer pricing and fees at the proposed \$6.50/GPU-hour rate.
Acceptance and exit	Workload acceptance, service start, contract duration, deposits, service credits, remedies and termination.

Proposed agreement scope. No deposit, minimum payment or take-or-pay commitment is established. Marketplace access does not guarantee customer receipts.

A long-term home for the operation

50 years

site-use agreement, signed status confirmed by management

Management identifies BC LLC as landholder, with an ownership connection to the CEO. The property is reported paid off.

39.39 acres / 5,035 sq ft gross A + C area

1% annually

Management describes a payment to BC LLC of 1% of profit remaining after expenses.

The written profit definition, premises, termination, improvements and financing rights remain unreviewed.

Owner record: agreement signed, document and title unreviewed. Site access does not imply SmartTec property ownership or investor collateral. Runway campus concept.

Power is a potential operating advantage

<7 cents

per kWh, reported by management

Solar + batteries + gas generation

Management reports a supply agreement.
Its delivered cost advantage remains
subject to firm capacity, reliability and
complete operating costs.

Outstanding supply terms

Exclusive continuous kW

Service availability date

Fuel and maintenance obligations

Losses, replacements and equipment costs

Interruption and recovery terms

The rate is not a verified all-in tariff. Shared OG&E service is recorded separately; it does not establish exclusive capacity. Runway power concept, not installed equipment.

Eight complete Supermicro B300 systems

\$5.36m

8 systems x \$670,000

64 proposed GPUs

60 saleable + 4 financial reserves

Direct liquid cooling

Owner-reported complete-system scope

Eight B300 GPUs

Dual Intel Xeon 6776P CPUs

NVSwitch fabric


Networking and storage

NVIDIA software stack and support

Supplier price and scope are management inputs. Exact configuration is private and unreviewed. Support term, external fabric, taxes, freight and installation remain unreconciled.

60 saleable GPUs. Four financial reserves.

EIGHT SYSTEMS / EIGHT GPUS EACH

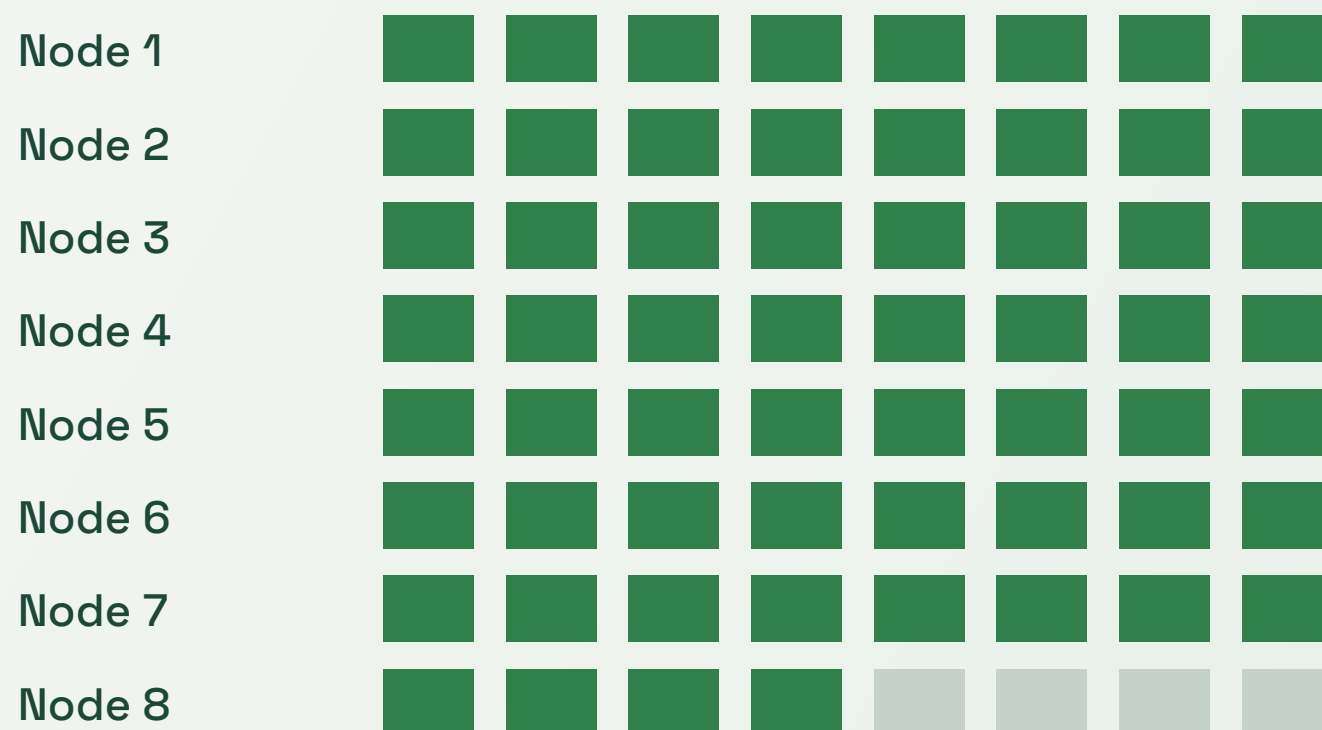

60 saleable

Revenue uses the 60 saleable GPUs.
All 64 are in the proposed purchase.

Reserve is not full redundancy

Four GPUs cannot replace one complete eight-GPU node. Whole-node scheduling and recovery capabilities remain unvalidated.

Illustrative financial allocation, not an approved scheduling or spare-parts topology. Heat and electrical design must account for the complete proposed fleet.

One building. Two controlled cooling loops.

225 kW

net cooling-duty screening target
per full-duty chiller

Two full-duty chillers and two CDUs are retained in the initial comparison. The proposed duty criterion retains required cooling with one unit unavailable.

Warm server-coolant circuit

CDUs isolate and control the compatible direct-liquid-cooled server loop.

Separate residual-air cooling

The residual-air design compares rear-door cooling with complete new room cooling. The building has no working air conditioning.

225 kW is an engineering allowance, not confirmed OEM load: $(8 \times 20 + 20 \text{ ancillary} + 5 \text{ pump}) \text{ kW} \times 1.20 = 222 \text{ kW}$, rounded up. Component redundancy is not facility certification.

Cooling: complete installed cost scenarios

\$1,083,600

Full-scope analyst comparison. Two chillers, two CDUs, dry coolers, four active rear doors and installation allowances. Includes 20% contingency.

\$831,600

Lower-cost sensitivity. Assumes a \$100,000 chiller pair and defers \$70,000 of separate dry coolers. Other allowances and 20% contingency remain.

Neither amount is minimum pricing or an approved contractor bid.

New and warranted refurbished equipment are options under assessment. Both require summer duty, residual-air cooling, controls, installation and commissioning.

Savings are arithmetic, not verified quotations. Deferred dry cooling changes seasonal energy use. The team reports a mechanical contractor, electrician and plumber are available.

Partial initial capital requirements

CURRENT PLANNING INPUT	FULL-SCOPE	LOWER-COST
Eight complete B300 systems	\$5,360,000	\$5,360,000
Cooling allowance	\$1,083,600	\$831,600
Retained startup/acquisition allowance	\$566,000	\$566,000
Retained opening operating reserve	\$264,501	\$264,501
PARTIAL INITIAL FUNDING	\$7,274,101	\$7,022,101
Above initial \$6m founder funding	\$1,274,101	\$1,022,101

Excludes remaining non-cooling site work, reserve revisions and later capital calls. The cooling scenarios replace the earlier \$652,800 combined site allowance; scope overlaps remain unresolved.

GPU rental revenue illustration

\$2.85m

illustrative annual gross billings

60 saleable GPUs x 20 paid hours/day
x \$6.50/GPU-hour x 365 days

From gross billings to project cash

Unpaid hours and customer collections

Platform or sales charges

Power, cooling and connectivity

People, support and maintenance

BC LLC payment, taxes and reserves

Uncontracted billing arithmetic, not a forecast or investor profit. 20 paid hours/day equals 83.3% utilization of saleable capacity. Actual utilization, collections, fees and net receipts remain unresolved.

Current return model status

Updated ROI: not established

The updated capital and operating cost basis remains incomplete. New cooling scope, remaining site work and the BC LLC payment are not yet reconciled into a definitive return model.

Capital inputs under review

Non-cooling site work, taxes, freight, installation, working capital and future reserves.

Operating inputs under review

Net receipts, seasonal power, maintenance, site payments, taxes and hardware-life costs.

Founder funding intent supports capital availability. Updated NPV, payback and investor distributions remain unestablished pending complete costs and commercial terms.

Historical model context

Previous model result

-\$0.67m

NPV at an assumed 15% annual hurdle

Positive operating cash did not compensate for the previous modeled capital cost and timing.

A superseded cost basis

The earlier model used a \$652,800 combined site allowance. It did not include the newly itemized cooling comparison, unresolved non-cooling scope or BC LLC payment.

Its ROI, payback and price thresholds describe the superseded case only.

Historical comparison only, reproduced by the monthly engine. The earlier 28.7% ROI is not a current project return.

Planned return sensitivities

SCENARIO	ANALYSIS SCOPE
Supported operating case	Signed net price and payment terms; validated cost scope; realistic commissioning and collection timing.
Lower demand and pricing	Fewer paid hours, rate pressure, customer concentration, churn and nonpayment.
Delivery and operating stress	Delayed launch, higher power/demand costs, repair events, outage credits and added working capital.
Hardware-life and exit stress	Overhaul versus replacement, funded reserves, resale downside, wind-down costs and investor cash rights.

These analyses are proposed for the completed model and agreed investor structure. Updated outcomes have not been established.

Proposed capital-release milestones

GATE	EVIDENCE	CAPITAL CONSEQUENCE
1 Commercial	Paid validation and enforceable payment terms from a creditworthy counterparty	Order size linked to supported demand.
2 Technical	Exact load/flow requirements, full installed budget and deliverable power/network	Delivery scope and reserves ready for approval.
3 Procurement	Final price, payment milestones, warranty, delivery and acceptance terms	Orders subject to documented release controls.
4 Service acceptance	Load tests, failure tests, customer acceptance and operating readiness	Service commencement, then receipt-led expansion.

A proposed control framework, not completed milestones or an approved procurement commitment. Staged orders remain subject to supplier and customer agreement.

Phased delivery to customer acceptance

WORKSTREAM	CURRENT BASIS	PROGRESSION MILESTONE
Building preparation	Single-building deployment planned; new cooling required	Survey, layout, permits and contractor scope.
Power	Owner-reported agreement and shared electrical service	Exclusive continuous kW and commissioning.
Cooling and network	Design concepts and contractor resources identified	Installed systems, measured duty and throughput.
Compute service	64-GPU planning fleet; customer discussions active	Workload proof, signed terms and customer acceptance.
Expansion	Potential demand under discussion	Evidence-backed next order and available capacity.

Earlier construction, utility and fiber dates remain unconfirmed targets, not completed work. No updated service launch date is committed in this presentation.

The team carrying the project forward

Syed Hussain

Chief Executive Officer

syed@z1power.com

Yasir Jahangir

Chief Technology Officer

yasir@smarttec.dev

[Credentials](#)

Muhammad Siddiqui

Chief Operating Officer

muhammad@z1power.com

Ryan

Director of Operations

ryan@smarttec.dev

Javed Iqbal, PhD

Strategic Advisor

javed@z1power.com

Shahab Kazmi

Senior Advisor

shahab.kazmi@estelleslighting.com

Ali Askari

Graphics and Media Relations

ali@z1power.com

Ken

Legal

Daniel

Chief Financial Officer

daniel@z1power.com

Yasir Jahangir: [NVIDIA AI Infrastructure](#) / [Google Cloud Architect](#) / [Google Cloud Network Engineer](#) / [PMP](#). Credly verified, 12 Sep 2026. Personal credentials; project experience and commitment levels remain unreviewed.

Investor participation and governance

Capital and economic rights

Potential terms cover the funded entity, founder equity or loan treatment, valuation, ownership, distributions and capital calls. No terms are fixed.

Site and related-party protections

BC LLC site rights and the annual profit payment are material to the structure. Improvements, termination, assignment and financing rights remain unreviewed.

Reporting and oversight

Proposed reporting covers receipts, utilization, outages, costs and reserves. Milestone approvals and related-party protections remain subject to agreement.

Governance proposals require agreement and documentation. Paid-off property is not automatically SmartTec equity or investor collateral. No preferred return or waterfall is promised.

Proposed execution responsibilities

PROPOSED LEAD	RESPONSIBILITY SCOPE
CEO / COO	Customer counterparty, paid workload evidence, minimum payments and staged capacity commitments.
CTO / Operations	Supplier interfaces, liquid-cooling requirements, network design, service tests and operating procedures.
Mechanical / Electrical / Plumbing	Complete installed pricing, design coordination, site scope and tested commissioning.
CFO / Legal	Founder contribution documents, BC agreement review, full model, reserves and investor terms.

Proposed responsibilities; assignments are not yet confirmed. Contractor availability is owner-reported; qualifications, scope, prices and acceptance remain to be established.

Customer-led growth options

64 GPUs under review

Eight systems form the current planning case. Customer commitments and the completed cost model determine what is purchased and when.

180 GPUs discussed

Management reports potential customer interest at this scale. It is not signed demand, funded expansion or approved site capacity.

Owned compute or customer-owned hosting

The two routes carry different capital needs, customer credit exposure and service obligations. Current revenue arithmetic excludes hosting and manufacturing income.

Runway campus concept, not installed buildings or approved expansion plans. Future manufacturing and energy development require separate budgets and decisions.

Principal risks and dependencies

EXPOSURE	CURRENT DEPENDENCY
Commercial	No signed payment obligations. Credit support, workload requirements and acceptance remain open.
Power and cooling	Delivered capacity, all-in tariff scope, summer duty and failure performance remain unverified.
Equipment and operations	External fabric, support term, staffing, security and replacement funding remain unreconciled.
Property and governance	BC agreement and title unreviewed; payment base, contributions and investor rights remain unresolved.
Financial information	Incomplete costs and no definitive updated return. Audited company statements have not been reviewed.

Development-stage discussion material. Capital remains at risk. No audited SmartTec financial statements, investment approval or funding guarantee is represented.

Financial assumptions and cost boundaries

Energy and maintenance

The historical model included facility overhead energy through PUE 1.4 at 7 cents/kWh. Seasonal cooling energy and site charges remain unreconciled within that cost basis.

Commercial and property costs

Net host receipts, customer fees, collections and the BC LLC profit-payment definition remain open. Tax, reserve and distribution treatment are unresolved.

Reserves and service coverage

The \$264,501 opening reserve and \$25,000/year cooling-service allowance are planning inputs. Supplier-covered and incremental costs remain unreconciled.

No revised operating-expense total or five-year cash schedule is asserted. Exact supplier support coverage, other site work and later capital requirements remain open.

Information basis and sources

Management inputs / 11 Sep 2026

Founder capital and overage willingness

Supermicro complete-system price and scope

BC LLC signed-site-agreement status

One-building deployment; no working HVAC

Active customer discussions; no signed terms

Analyst work / preliminary

Itemized cooling comparison, arithmetic funding bridge and historical monthly cash model. No contractor bids.

External sources provide product or market context only. Owner facts are reported; private contracts, quote terms and funding have not been independently reviewed.

External context, not project verification

Supermicro liquid-cooled Blackwell portfolio

Vast.ai hosting and marketplace context

New chiller manufacturer pricing context

Refurbished chiller testing and warranty

SmartTec investor room and planning basis

Discuss the first SmartTec deployment

A proposed founder-backed B300 deployment

SmartTec invites prospective investors to discuss its B300 proposal, customer pipeline and participation structure. The discussion brings together commercial terms, installed costs and investor rights.

Participation structure and investment terms remain open.

Yasir Jahangir

Chief Technology Officer

yasir@smarttec.dev
918-520-3823

smarttec.dev/investors

8460 US 70, Mead, Oklahoma 73449. Discussion material; no definitive investment terms or return are offered. Background: Runway campus concept.
