



Compute with a place to grow

SMARTTEC / MEAD, OKLAHOMA

Shared AI inference. Dedicated GPU servers.
A grid-first deployment, built around customer commitments.

INVESTOR PRESENTATION / MODEL 2026.09-target



A focused first deployment

\$6.00m

initial founder capital, owner-reported

Management intends to fund the overage.
Contribution timing, form and transfers
require documentation.

A tangible starting point

Long-term site access in Oklahoma

Eight proposed Supermicro systems

Two ways to sell owned GPU capacity

Growth linked to paying customers

The economic discipline

The current target projects 9.78% IRR. Rental utilization, sustained pricing and delivered cost determine the return; it remains below the 15% hurdle.

Founder capital is reported, not independently verified. The current proposal is a development-stage investment discussion.

Two offerings. One owned compute fleet.

Shared AI inference

A multi-tenant service using SmartTec-owned GPUs. Planned customer access is through managed inference endpoints, with workload isolation, metering and support.

Dedicated GPU servers

Single-tenant access to agreed SmartTec-owned server capacity. Reserved compute for inference, model development, rendering and other validated GPU workloads.

One capacity and revenue budget

The same GPUs cannot earn twice at the same time. The financial model uses GPU-hours; it assumes no additional token-sales or platform-margin uplift.

Proposed offerings, not a claim of an operating service. The shared/dedicated allocation, product pricing, security controls and customer SLAs remain to be validated.

Clear ownership. Clear revenue boundaries.

SERVICE	WHO OWNS THE HARDWARE	TREATMENT IN THIS MODEL
Shared AI inference	SmartTec	Part of the same owned fleet; no separate per-token revenue forecast.
Dedicated GPU servers	SmartTec	Capacity monetized as GPU-hours; contract cases reserve a defined paid allocation.
Colocation / hosting	Customer	Separate potential business. Customer-owned hardware and hosting revenue are excluded.
Solar and BESS	Separate project scope	Future hybrid power investment; no savings or revenue in the grid-only target.

Dedicated server configurations and service commitments must match whole-node scheduling and recovery capabilities. Service mix is not an additional revenue multiplier.

Marketplace access. Rental-led revenue.

Three-year access

Management reports a signed three-year marketplace-access relationship. The platform retains 20% of rental revenue.

Current commitment level

Paid only for rented GPU-hours

90% paid utilization target

No guaranteed minimum receipts

Convert access into paid hours

At \$6.50 per GPU-hour, \$5.20 remains after the marketplace fee and before all other costs. Access is not a take-or-pay customer contract.

Agreement status is management-reported; not independently reviewed. Flat pricing and continued channels in Years 4–5 are assumptions, not guaranteed contracted receipts.

A long-term operating location

50 years

site commitment; signed status
owner-reported

BC LLC owns the property and has an
ownership connection to the CEO.
SmartTec holds site rights; land value is
not included as SmartTec cash equity.

1% annually

BC LLC share of the agreed profit base

Management describes profit after
expenses. The model uses its selected
accounting-profit basis; the operative
agreement, consent rights and payment
definition remain unreviewed.

Property is reported paid off. Premises, assignment, improvements, termination and financing rights require document review. Runway campus concept, not proof of installed capacity.

Grid first. Hybrid power in a later phase.

9.5 cents

per kWh energy planning assumption

Launch uses grid power. The model includes energy and demand charges separately, with demand based on the estimated billed peak.

\$12/kW

monthly demand-charge assumption

Solar and battery storage are future additions. They require their own installed budget, tariff analysis, interconnection and measured savings.

Neither tariff component is verified. The billed peak is 90.00% of the design-day peak. No behind-the-meter discount or solar savings is included in the target. Runway hybrid-power concept.

Eight complete B300 systems

\$5.36m

8 systems x \$670,000

64 GPUs installed

60 revenue-producing GPU allocation

4 installed GPUs held uncommitted

Supermicro HGX B300 platform

Eight GPUs per complete system

Dual CPUs and NVSwitch fabric

Networking and local storage

NVIDIA software and support


Earlier air-cooled cost allowance

Support: 36 operating months included; then 5.00% of complete-system purchase cost/year before 3.00% annual cost escalation. Supplier terms are unverified.

Complete-system price and inclusions are owner-reported. Exact quoted SKU, inter-node fabric, support coverage and delivery terms require confirmation. The direct-liquid Buildings A/C design requires repricing.

Capacity allocation is not full redundancy

EIGHT SYSTEMS / EIGHT GPUS EACH

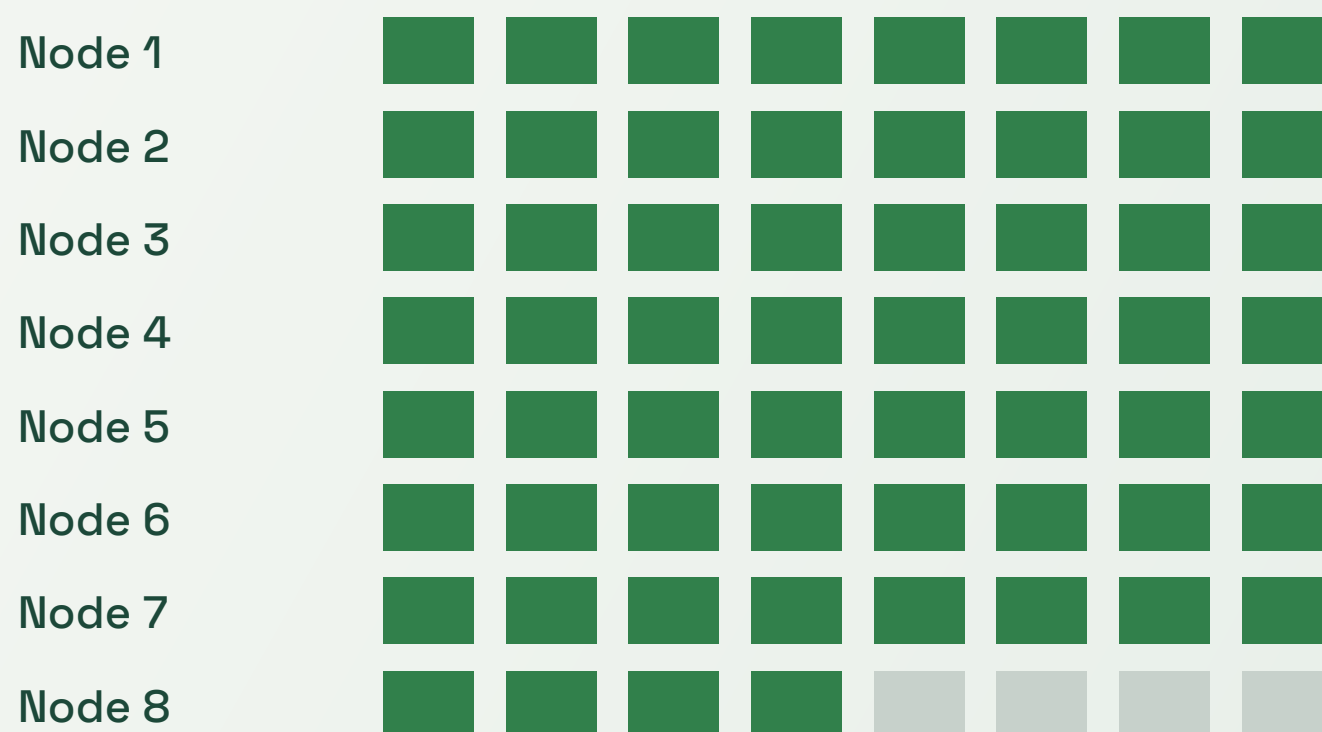

60 modeled earning GPUs

All 64 GPUs are purchased. The four held-back GPUs are installed but unsold, not loose spare cards.

A whole node contains eight GPUs

One failed node leaves 56 installed GPUs. Maintaining a 60-GPU customer commitment needs a separately designed recovery plan.

Illustrative capacity allocation, not an approved tenant layout or guaranteed uptime. Customer SLAs, service credits, standby capacity and recovery time must be agreed before commitments.

Power and cooling sized together

128.4 kW

IT load at full modeled draw

2 x 50-ton chillers

5 x 40 kW in-row coolers

203.2 kW

estimated whole-site design-day load

40.2 tons of design cooling duty. These retained air-cooled budget quantities include spare units. Direct-liquid racks and residual room heat require revised engineering and pricing.

Node load 15 kW is an estimate. Chiller ambient/glycol derate, electrical ratings, pumps, controls, transfer, fire/egress and layout need engineer/vendor approval. N+1 arithmetic is not facility certification.

The initial capital requirement

USE	AMOUNT	BASIS
Complete GPU systems	\$5,360,000	Owner-reported complete-system price
Storage / management / spares	\$80,000	Additional allowance; quote overlap unresolved
Freight / rigging / sales tax	\$163,200	Planning allowance; exemptions unverified
Power / cooling / site infrastructure	\$782,499	Includes engineering and contingency
Cash reserve and launch top-up	\$591,312	Includes receivables funding
TOTAL INITIAL FUNDING	\$6,977,011	Model v2026.09-target target; not a contractor quotation

Above the initial owner-reported \$6.00m is \$977,011. Management intends to cover the overage. Capital availability and terms remain unverified.

Operating profit and capital return differ

\$3.07m

Year 2 modeled revenue

60 earning GPUs x 8,760 hours
x 90.00% paid utilization
x \$6.50/GPU-hour in Year 2

\$1.81m

Year 2 EBITDA / before tax and depreciation

The target holds \$6.50 flat for five years and charges a 20% fee on all rental revenue. Cash costs also include staff, support, power, tax and site payments.

Utilization and price are assumptions, not customer commitments. Positive EBITDA does not establish investment payback or cash available to an outside investor.

Five years of target operating performance

YEAR	REVENUE	OPERATING COST	EBITDA	OPERATING CASH
1	\$2.82m	\$1.19m	\$1.63m	\$1.51m
2	\$3.07m	\$1.27m	\$1.81m	\$1.64m
3	\$3.07m	\$1.29m	\$1.79m	\$1.63m
4	\$3.07m	\$1.57m	\$1.50m	\$1.42m
5	\$3.07m	\$1.63m	\$1.45m	\$1.38m

Operating cash is after modeled operating tax and the BC LLC payment. It excludes asset sale proceeds and reserve release.
The launch period is 1 months. Receivables, funded reserves and actual distribution timing are handled separately in the dated project-cash schedule.

The current target projects positive returns

9.78%

headline project IRR / primary metric

15.00%

modeled project-return hurdle

\$7.58m total operating cash over five years

This exceeds initial funding before terminal recovery. The 9.78% headline includes asset resale and reserve release, and remains below the 15% hurdle.

Headline NPV at 15.00%: -\$0.93m / Headline cash multiple: 1.352x including modeled resale

Five-year hold; resale assumes 20.00% of hardware cost and 50.00% of infrastructure, with no guaranteed buyer. Annual-funded IRR 9.77% and dated XIRR 9.76% are timing diagnostics, before investor allocation.

Customer economics change the result

PHASE-1 CASE	INITIAL CAPITAL	YEAR 2 OPERATING CASH	HEADLINE IRR
Target / flat price	\$6.98m	\$1.64m	9.78%
Slower ramp	\$6.91m	\$1.74m	7.04%
Price pressure	\$6.98m	\$1.46m	3.46%

Target: 90% paid use and flat \$6.50. Slower ramp: 55% in the first eleven operating months, then 90%. Price pressure: 90% use with 10% annual price decline.

All cases retain the 20% fee and other cost methods. Conditional projections; none clears the 15% hurdle. The 240-GPU sensitivity uses historical inputs, not these target assumptions.

Three years of access is not five-year revenue

20%

marketplace deduction on all rental billing

The target assumes \$6.50 per rented GPU-hour throughout the five-year hold. No price protection or minimum rental volume has been established.

90%

paid utilization target, not measured uptime

Management reports a signed three-year access relationship. Years 4–5 assume continued access or replacement sales channels; renewal is not confirmed.

Planned billing starts November 1, 2026. Fees, customer credit, collections, service acceptance, availability and realized occupancy determine actual receipts.

Operating cash supports capital recovery

\$1.64m

Year 2 modeled operating cash

-\$0.93m

headline NPV at 15.00%

Every target forecast year shows positive modeled operating cash after operating tax and the BC LLC payment.

The \$6.98m initial outlay, flat target pricing and modeled exit value produce a 9.78% headline project IRR. Annual cash generation alone does not establish full capital recovery.

Conditional rental target. Includes modeled resale and reserve release. Unlevered project return before any investor ownership, preference or distribution waterfall; not a promised return.

Release capital against delivery milestones

STAGE	DELIVERABLE	DECISION BASIS
Commercial validation	Paid workload evidence and enforceable reserved-capacity terms	Customer economics, credit support and service acceptance
Engineering and site	Utility capacity, layout, electrical and cooling selections	Complete installed scope and commissioning criteria
Procurement	Confirmed system specification and supplier milestones	Price validity, support dates, delivery and acceptance
Commissioning	Load, cooling, network and recovery tests	Measured service performance before customer acceptance
Operating growth	Utilization, receipts, support and reserve reporting	Further purchases linked to supported demand

Planned first billing: November 1, 2026. Funding assumed October 1; one pre-revenue month. Delivery, staffing and commissioning power begin in month 1. Schedule requires confirmation.

The team carrying the project forward

Syed Hussain

Chief Executive Officer

syed@z1power.com

Yasir Jahangir

Chief Technology Officer

yasir@smarttec.dev

[Credentials](#)

Muhammad Siddiqui

Chief Operating Officer

muhammad@z1power.com

Ryan

Director of Operations

ryan@smarttec.dev

Javed Iqbal, PhD

Strategic Advisor

javed@z1power.com

Shahab Kazmi

Senior Advisor

shahab.kazmi@estelleslighting.com

Ali Askari

Graphics and Media Relations

ali@z1power.com

Ken

Legal

Daniel

Chief Financial Officer

daniel@z1power.com

Yasir Jahangir: [NVIDIA AI Infrastructure](#) / [Google Cloud Architect](#) / [Google Cloud Network Engineer](#) / [PMP](#). Credly verified 12 Sep 2026. Personal credentials, not SmartTec corporate certification.

Price the risk as well as the GPU

Reserved customer capacity

Contracted price, minimum paid hours, service start, payment dates and counterparty support define the revenue commitment. Dedicated server shape must match the hardware allocation.

Merchant and shared inference

Usage, realized price, platform fees and workload mix determine receipts. Retail GPU list prices are context; they are not SmartTec net receipts or long-term customer contracts.

A passing scenario is not an offer

Pricing needs margin for launch delay, outages, service credits, cost overruns and customer credit exposure. These terms require commercial negotiation.

Initial connectivity allowance: \$4,000/month; bandwidth, route diversity and SLA scope are unconfirmed. No extra token revenue is modeled. Customer resale requires an enforceable buyer payment obligation.

Solar and storage are a separate investment

Add resilience and power options in stages

Solar generation

Potential on-site production requires an EPC scope, interconnection review, credible production profile and tariff-based self-consumption value.

Battery storage

Capacity, dispatch, degradation, replacement and the actual demand tariff determine savings. A battery is not automatically a firm alternate source for the full cooling load.

No solar/BESS capex, incentive, savings or revenue is credited to the GPU target case. The future hybrid system requires its own approved investment case; grid supply supports launch.

Start with 64. Plan for up to 240.

240 GPUs

management infrastructure design target

Initial: 8 systems / 64 GPUs / 60 saleable.
Target: 30 systems / 240 GPUs / 225
saleable. Expansion adds 22 systems and
176 GPUs.

\$24.85m

historical v6.1.1 maximum funding

Historical v6.1.1 maximum IRR: 0.49%. Original
inputs; not the current 90%-utilization
target. Initial funding does not purchase the
expansion fleet.

Management design target, not commissioned capacity or engineering approval. Confirm power, liquid cooling, networking, customers and expansion funding. Reprice the liquid-cooled design; workbook maximum holds back 15 GPUs.

Project returns precede investor economics

Capital and ownership

Founder equity or loan treatment, outside capital, valuation, ownership and future capital calls remain open. The available founder funding is reported; it is not a verified bank transfer.

Distribution and protections

Preferences, cash distributions, investor controls, exit rights and related-party protections require documentation. The BC LLC site commitment and payment basis are material to that structure.

No investor waterfall is modeled

The quoted project IRRs do not establish an investor's return after ownership dilution, preferences, fees or distributions. Financing scenarios also carry repayment obligations.

No fixed raise, ownership percentage, preferred return or investor entitlement is offered in this presentation. Definitive terms require agreement.

Evidence that governs the investment decision

DEPENDENCY	REQUIRED EVIDENCE
Customer payments	Executed customer terms, credit support, paid capacity and acceptance; no reliance on unsigned resale demand.
Hardware and installed cost	Final configuration, scope, support dates, delivered cost and complete contractor budget.
Grid, cooling and service	Verified tariff/capacity, engineering selections, permits and tested recovery performance.
Site and capital rights	BC LLC agreement definition and consent rights; contribution, overage and investor documents.
Cash and exit	Collections, taxes, reserves, repayment and dated distributions; supportable resale and completed customer obligations.

Development-stage risks remain. The model is an auditable planning case; forecasts and check cells do not verify customers, bank balances, installed equipment or future sale proceeds.

A traceable financial and technical basis

Reviewed model 2026.09-target

Native Excel recalculation and independent checks support the target. Website and PDF share its values; the original workbook is unchanged.

Headline project IRR is the quoted return metric. Annual-funded IRR and dated XIRR use different cash-timing conventions and are shown only as diagnostics.

Workbook stays private

Source identity and values are retained in the protected model.

Supplier specifications and market prices provide context only. The system quote, utility tariff, customer obligations, funding and BC LLC documents have not been independently verified.

External context, not project verification

[Supermicro HGX B300 platform](#)

[NVIDIA DGX B300 reference specifications](#)

[Daikin Trailblazer chiller range](#)

[Runpod on-demand pricing](#)

[Nebius on-demand pricing](#)

[SmartTec protected investor area](#)

Build the first deployment with SmartTec

A place. A fleet. A customer-led plan.

SmartTec is developing owned compute for shared AI inference and dedicated GPU customers. The next step is to align binding customer economics, installed delivery scope and investor rights.

Grid first. Customer commitments. Evidence before expansion.

Yasir Jahangir

Chief Technology Officer

yasir@smarttec.dev

918-520-3823

smarttec.dev/investors

8460 US 70, Mead, Oklahoma 73449. Conditional project scenarios, not signed revenue or promised investor returns. Runway campus concept.
